

BETHEL PARK ELEMENTARY CENTER CONSTRUCTION UPDATE

10-14-2025



Massaro
CM SERVICES, LLC





- Bus Loop grading for paving






- E wing Northside long board and flashing complete



- Long board wrapping around into courtyard




- **Flashing installed on F wing followed after completion of window frames**

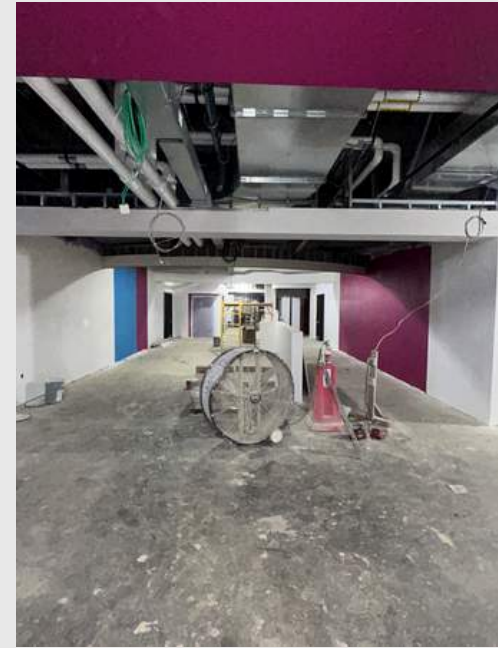

- **Ground floor E hallway painting**



- **Ground floor E classrooms casework and ceiling grid
(only needing floors and ceiling tile to complete)**

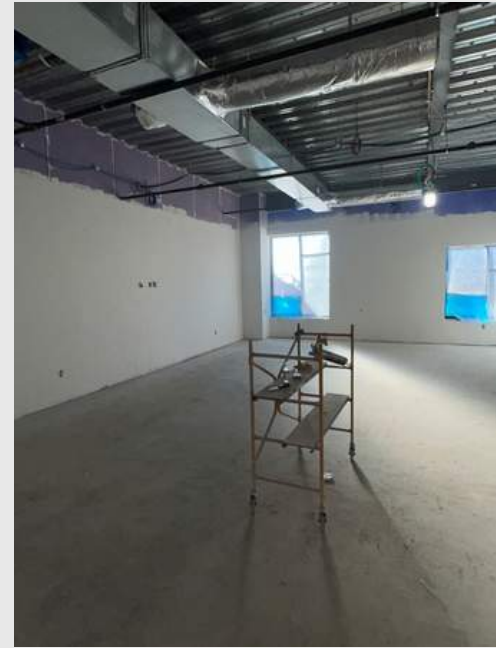

- **Ground floor F half of wing painted waiting for casework**



- Other half of F wing drywall and finishing



- **Ground floor A, C, and D hallway drywalled working on finishing**



- Completely roofed in



THANK YOU



Project Stats

- Safety = 440 Days with Zero Recordable Accidents

Upcoming Work

- Drywall and finishing 1st flr
- Finishing and painting ground flr
- Installing casework in ground flr E
- Installing a road around building
- Installing RTU's
